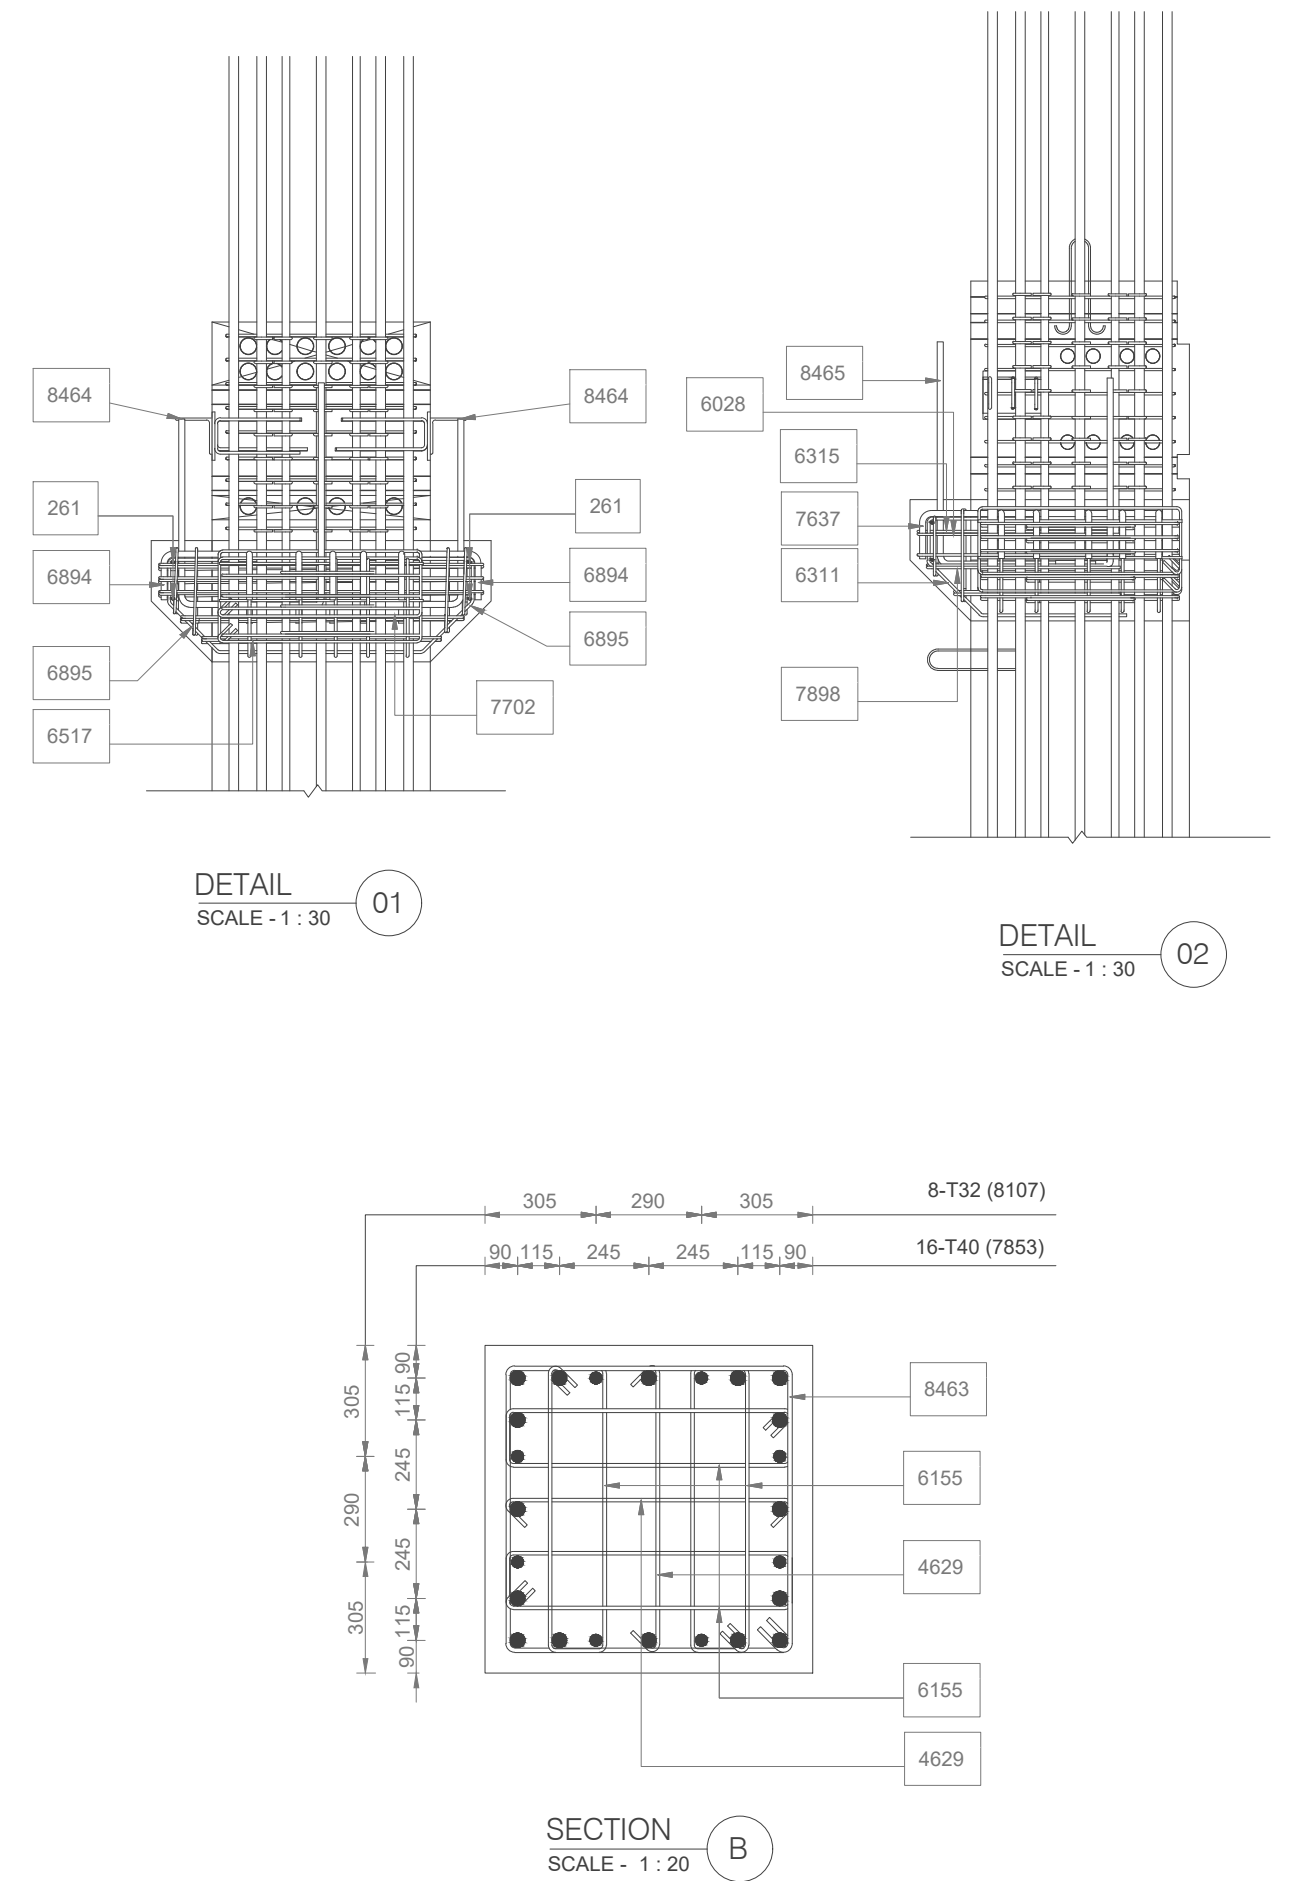
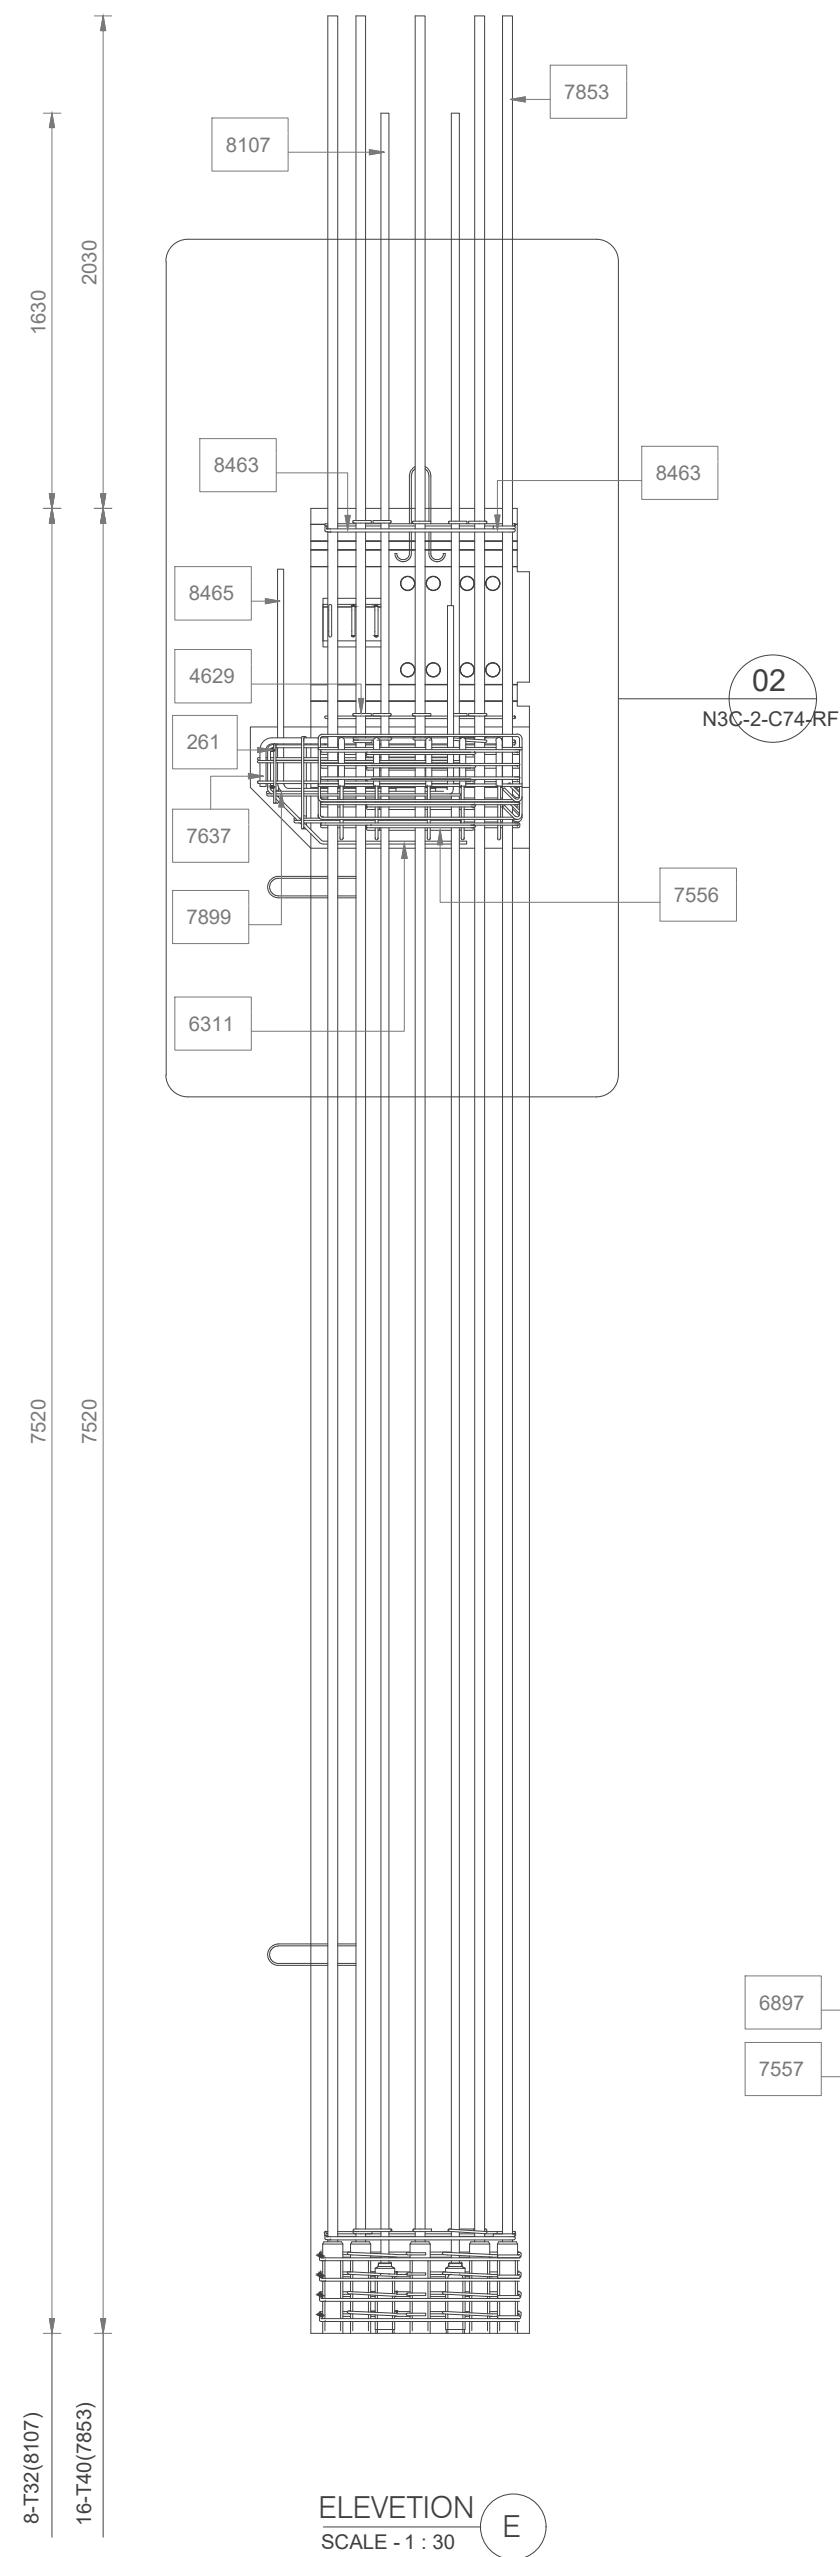
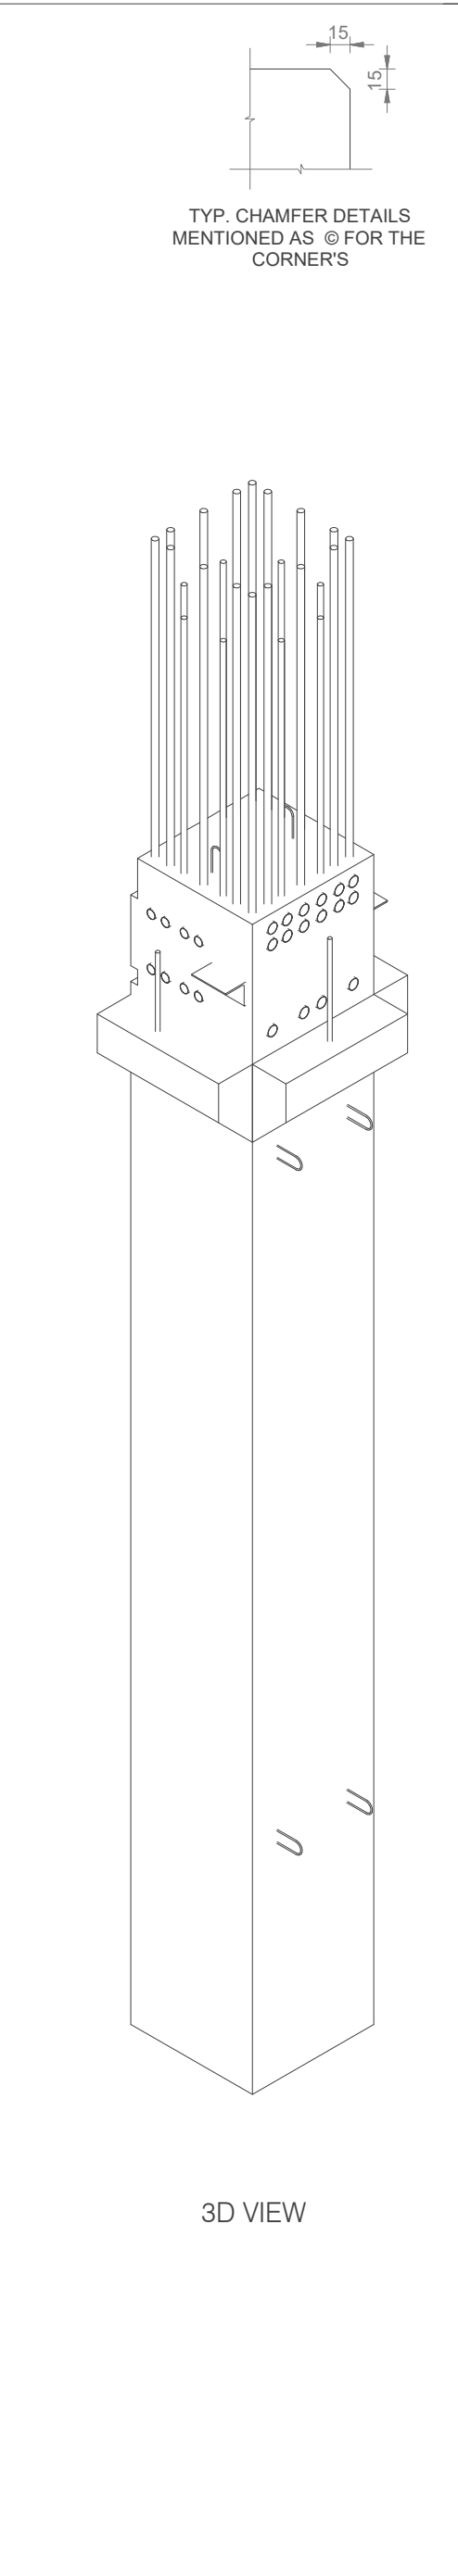
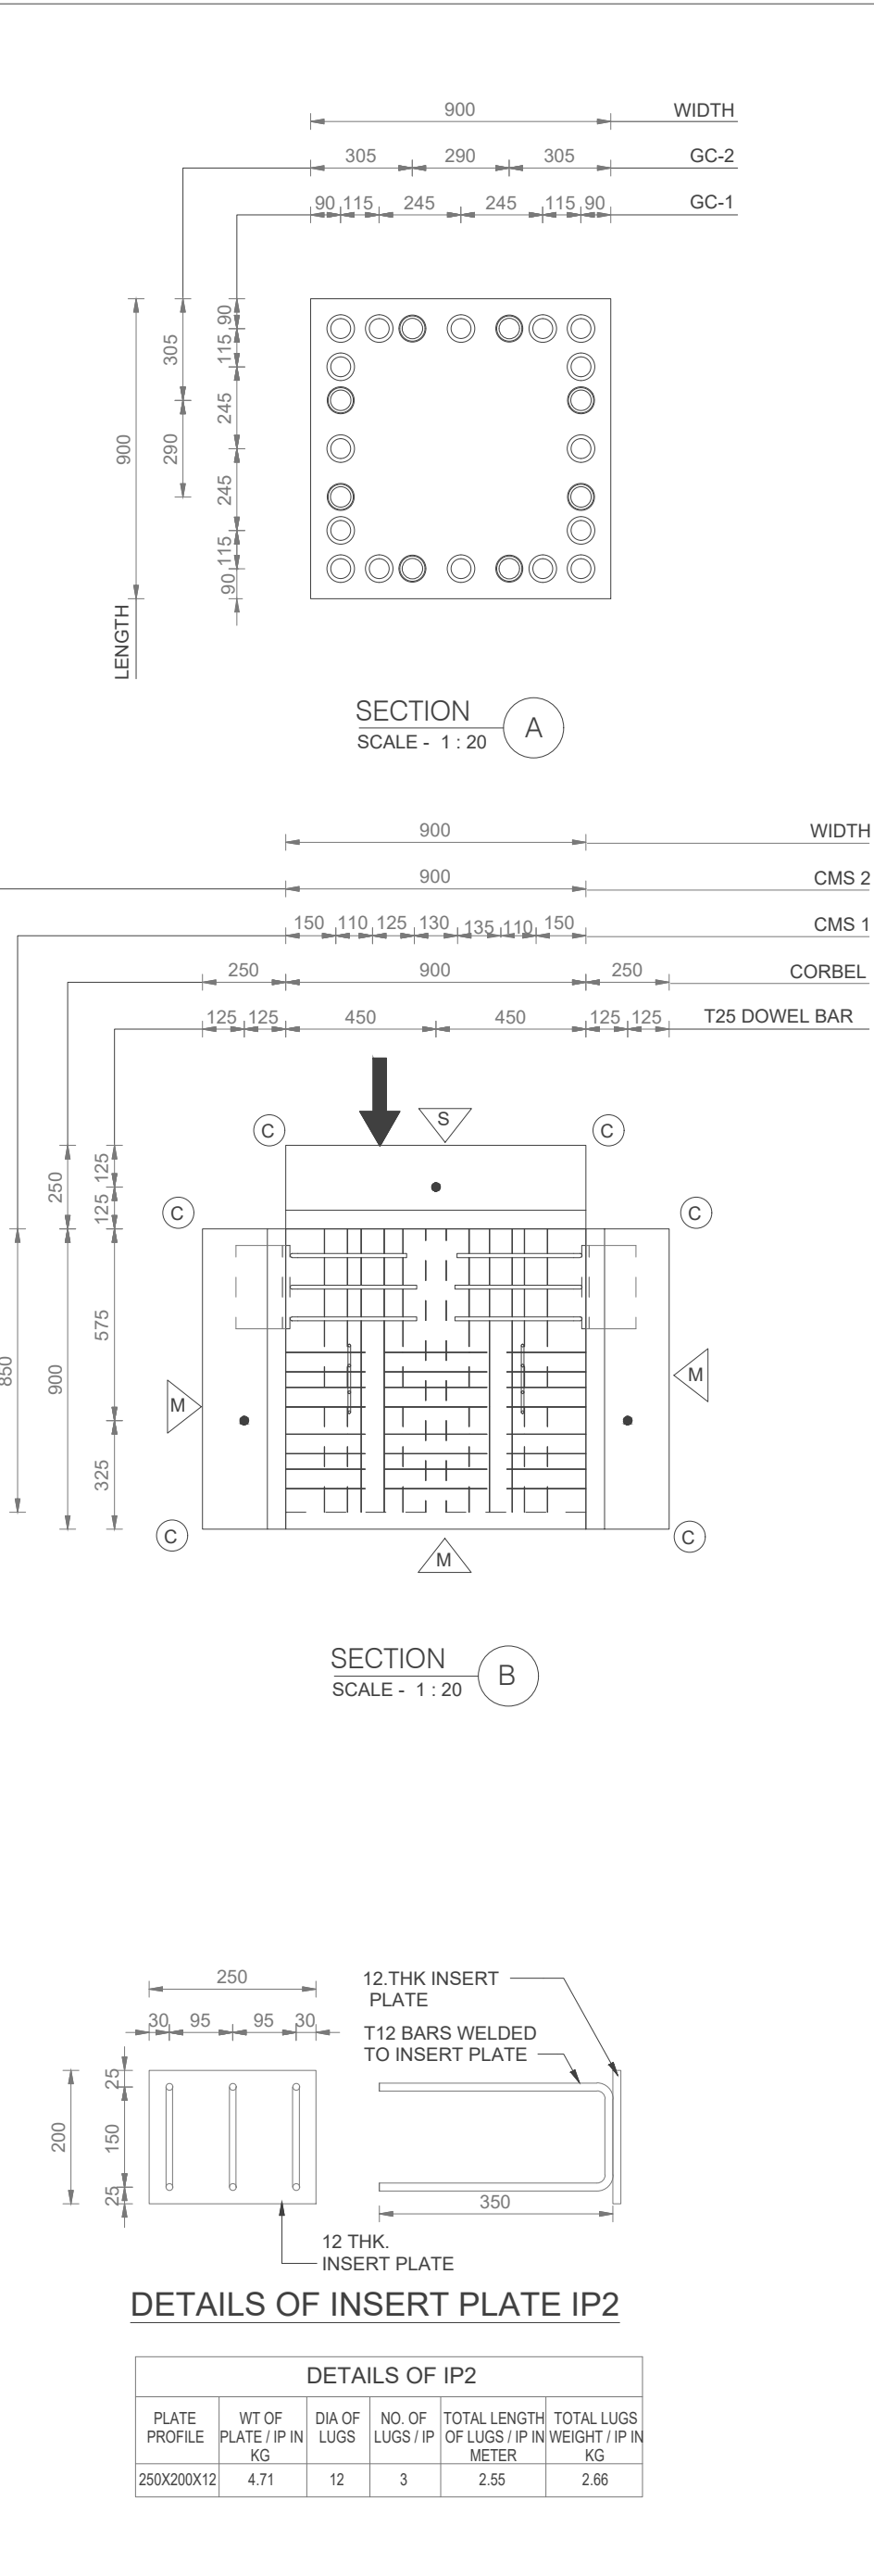
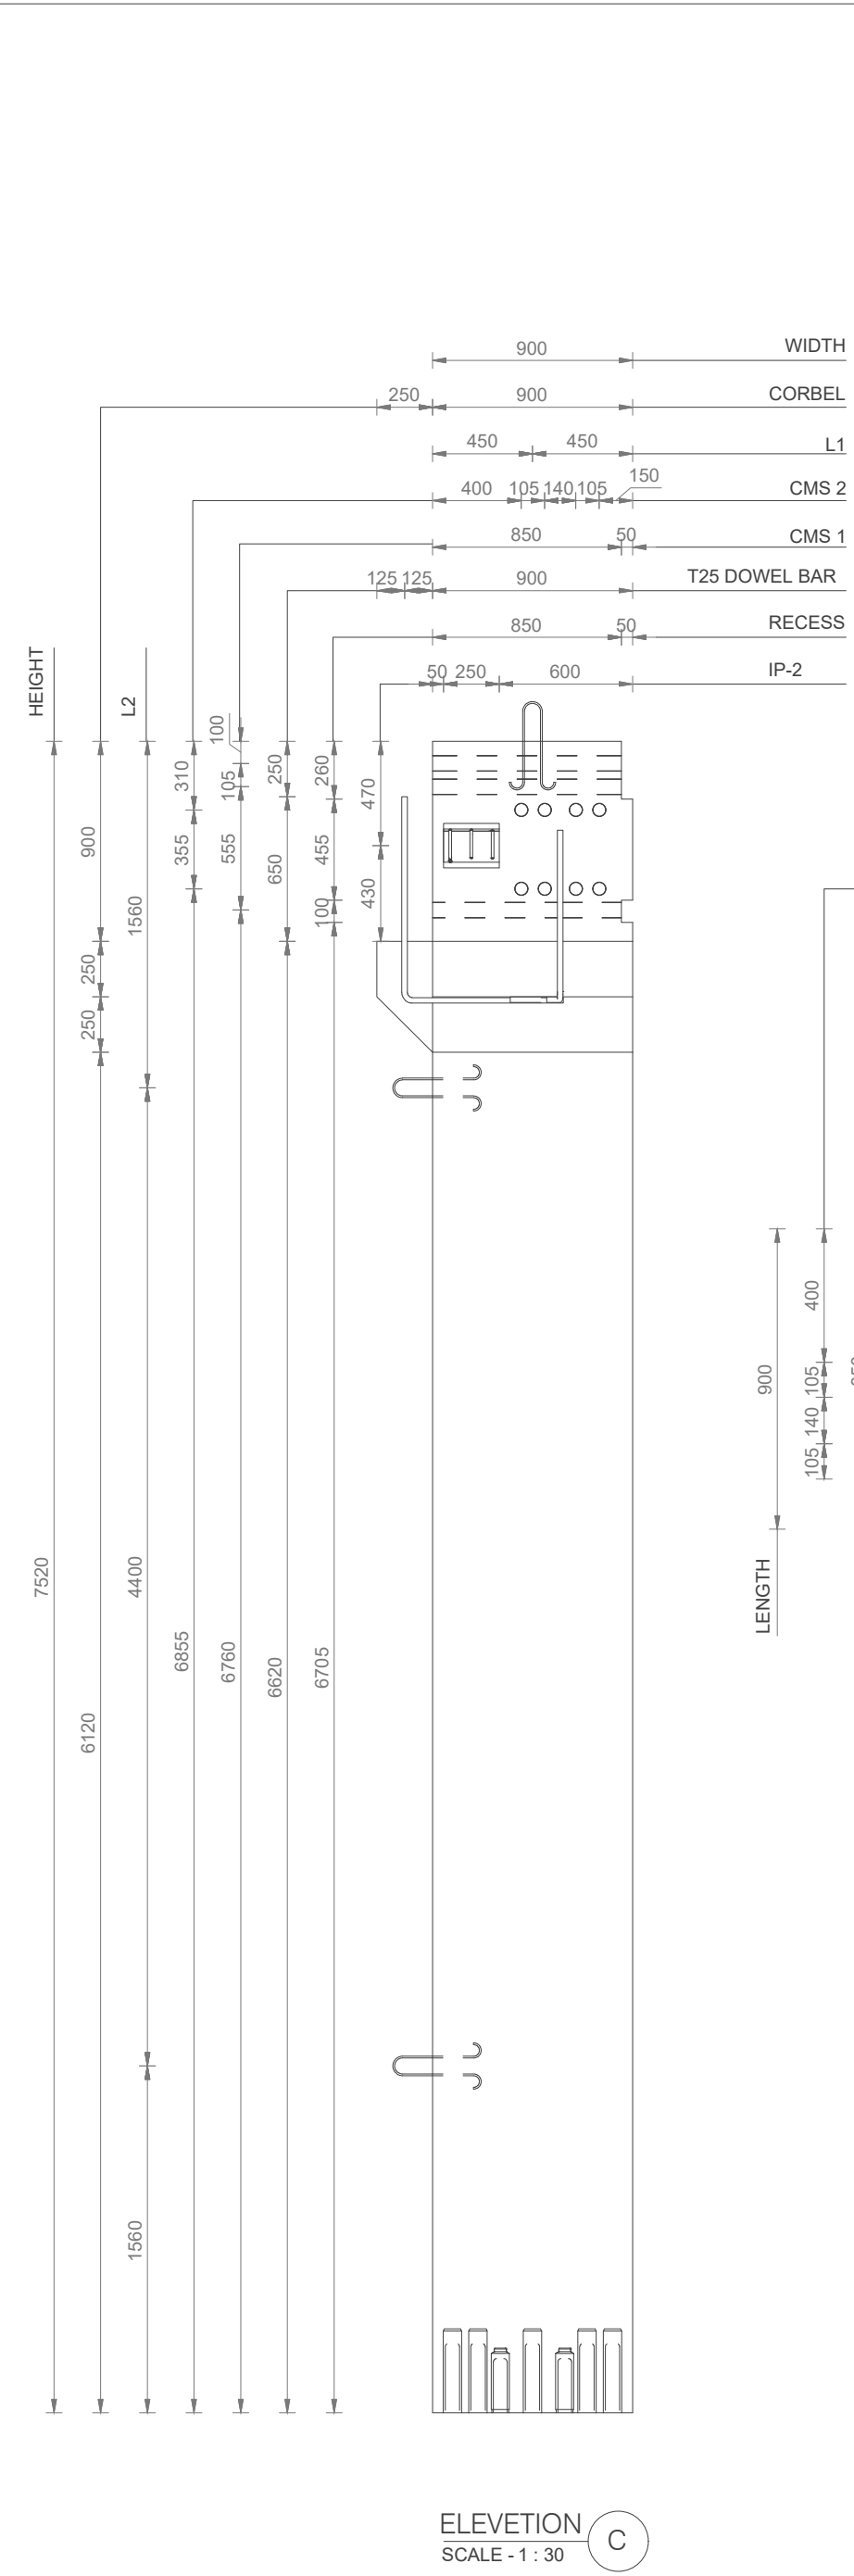
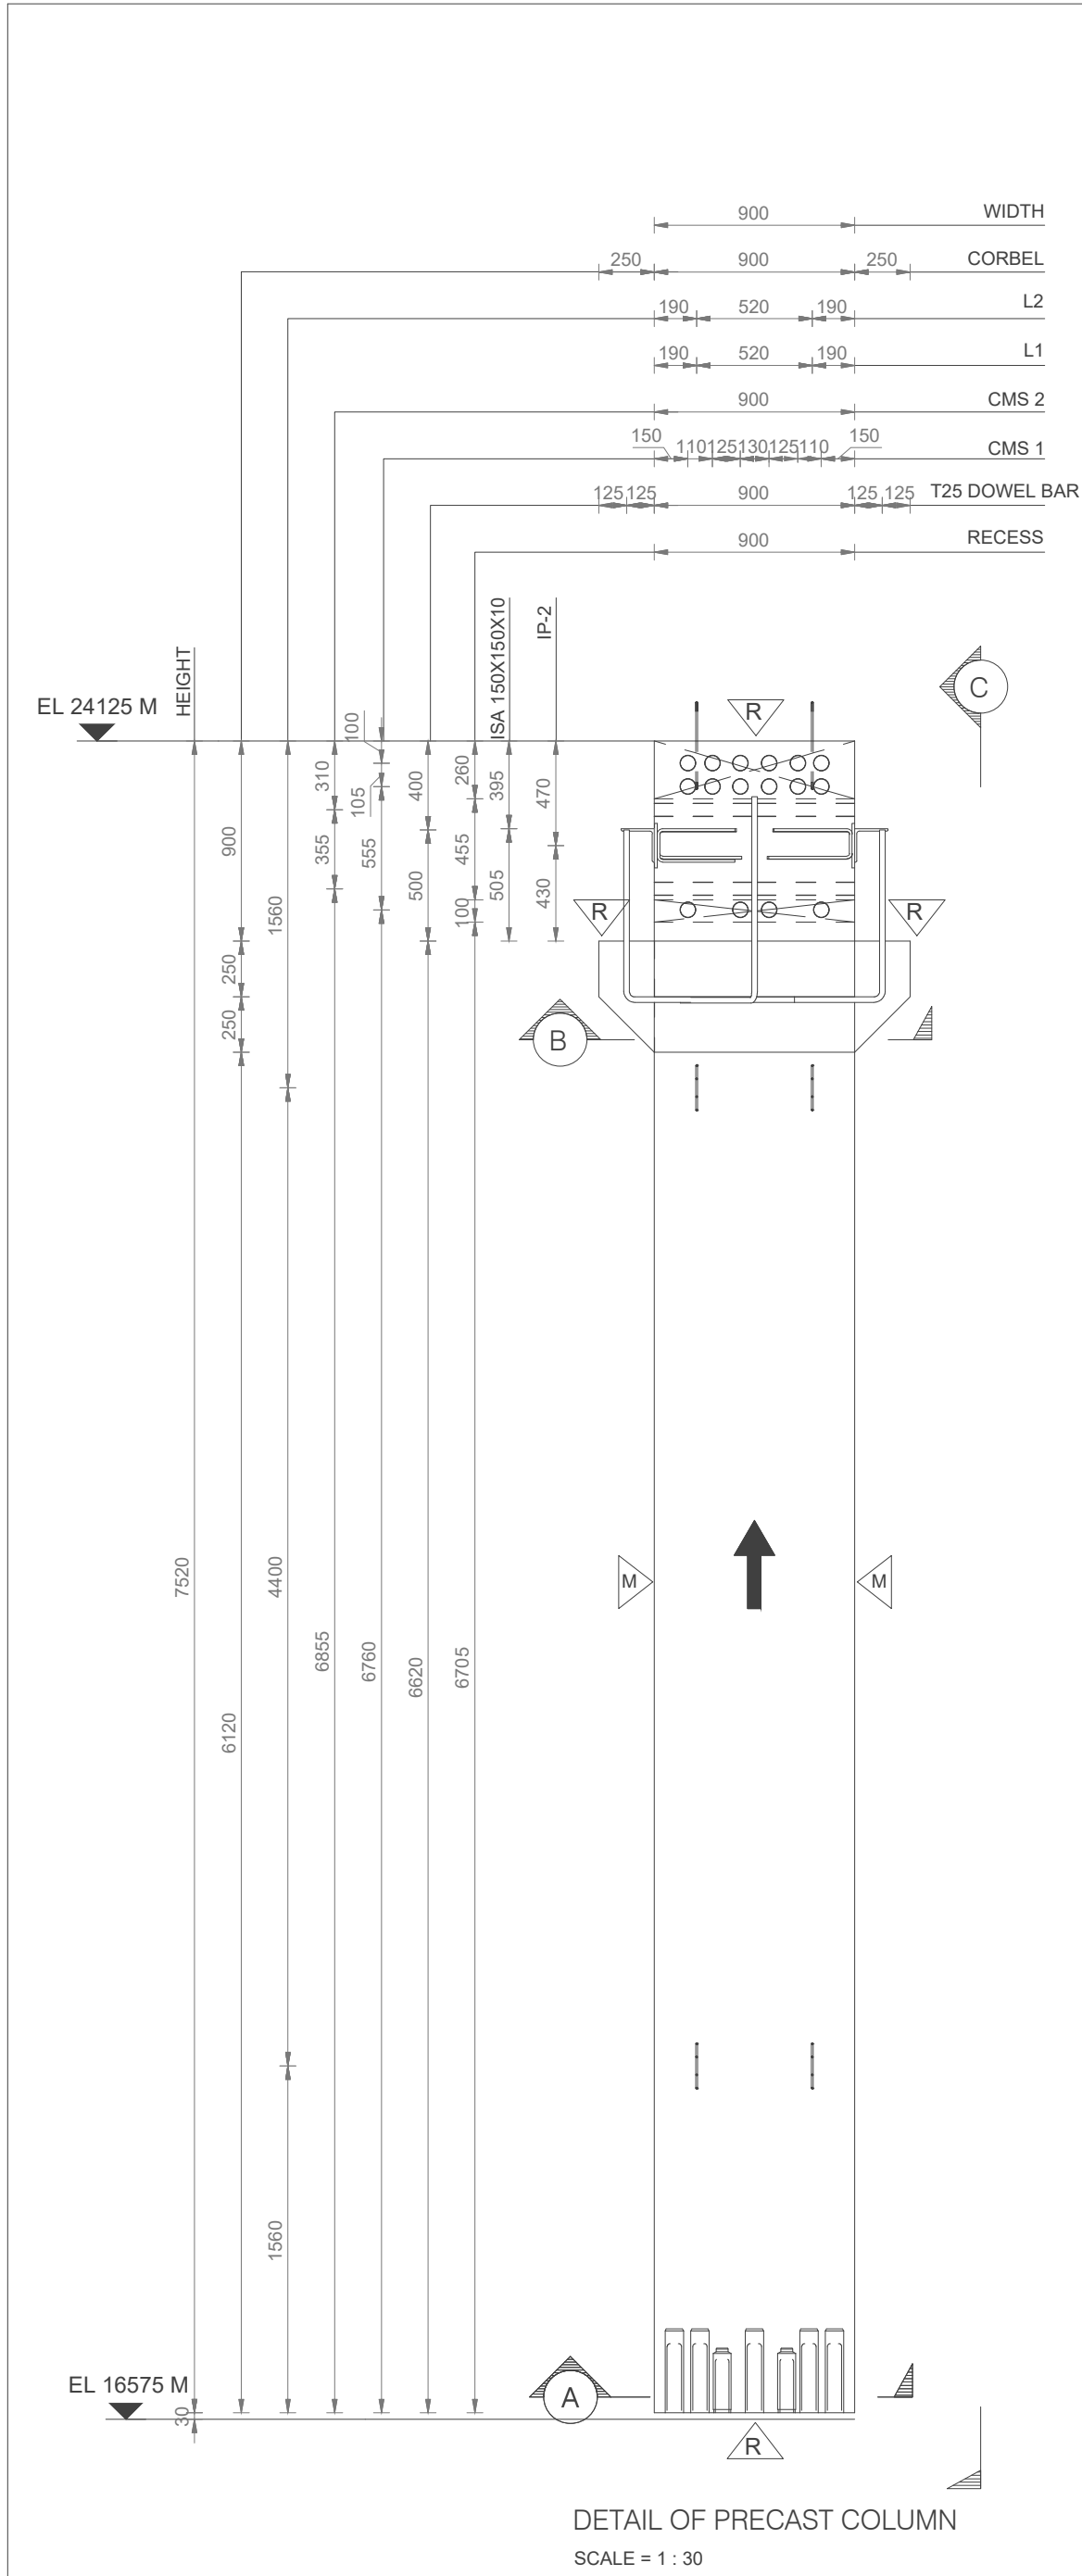




ELEVATION
SCALE - 1 : 30

R/O	25-06-2026	GOOD FOR CONSTRUCTION	NPS	SAM	SDK			
REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY			
REVISION HISTORY								
STRUCTURAL CONSULTANT :		PPS ENGINEERING CONSULTANTS LLP.						
		FIRST FLOOR, SERVICE BUILDING, BAFI BHAVAN, DR. MANIBHAI DESAI NAGAR, WARJE, PUNE 411058, INDIA. EMAIL : design@ppspl.in WEB SITE : www.ppspl.in Tel. : + 91 20 25232095						
PROJECT NUMBER		25-4035						
PROJECT NAME		ACXNNM-03						
 <i>Your Growth. Our Priority.</i>		CLIENT						
		ADANICONNEX						
REINFORCEMENT DETAILS OF N3C-2-C74								
PRECAST COLUMN :								
DWG NUMBER N3C-2-C74-RF								
RELEASED FOR _____	APPROVAL		NAME	DATE	SCALE	BY : R.O		
	TENDER		NPS	25-06-2026				
	CONSTRUCTION	☒	SAM	25-06-2026				
	NEGOTIATION	☒	SDK	25-06-2026	SIZE : A2			



LEGEND:-

- RAKED SURFACE - SMOOTH FINISH
 - MOULD FINISH - CHAMFER 15x15
 - ERECTION MARK / VIEW DIRECTION

NOTES:

- ALL DIMENSIONS ARE IN MM AND FOLLOW WRITTEN DIMENSIONS, DO NOT MEASURE.
- CLEAR COVER FOR :
A. PRECAST COLUMN = 60mm
B. PRECAST COLUMN CORBEL = 30mm
- GRADE OF REINFORCING STEEL, Fe 550D -TMT BARS CONFORMING TO IS1786:2008 WITH MINIMUM YIELD STRENGTH OF 550 N/mm²
- CONCRETE STRENGTH :
A. AFTER 28 DAYS : @ M70
B. DEMOULDING & LIFTING : @ M20
C. TRANSPORTATION & ERECTION : @ M50

DEMOULDING METHOD : HORIZONTAL

STACKING METHOD : HORIZONTAL

TRANSPORT METHOD : HORIZONTAL

ERECTION METHOD : NO. OF LIFFTER AS PER SHOP DRAWING

SITE NUMBER NM3 / 4 / 5

FLOOR LEVEL

UNIQUE ID

N3A-1-B1-1

BUILDING DGA - A
DGB - B
DC - C

ELEMENT MARK

	DESCRIPTION	QTY.
CMS-1	80 DIA CORRUGATED METAL SLEEVE	16
CMS-2	60 DIA PIC SLEEVE	8
GC-1	Ø40 GROUTC COUPLER 'S' TYPE	16
GC-2	Ø32 GROUTC COUPLER 'L' TYPE	8
IP-2	250X200X12 THK. PLATE	2
ISA150x150x10	ISA150x150x10	2
L1	LIFTER-15 TON CAPACITY EACH	2
L2	LIFTER-10 TON CAPACITY EACH	4
Grand total: 58		

PRECAST COLUMN VOLUME (M³)	PRECAST COLUMN WEIGHT (TONNES)
6.27	16.61

GI PIPE (OPTIONAL)

12.9 Ø STRANDS

PRECAST COLUMN

TYPICAL LIFTER DETAIL

(REFER STANDARRD LIFTING DETAILS DRAWING FOR LIFTER CAPACITY)

REFERENCE DRAWING

DRAWING NO.	DESCRIPTION
N3C-2-C74 -RF	REINFORCEMENT DETAILS OF PRECAST
N3C-2-C74 -RF1	REINFORCEMENT DETAILS OF PRECAST
COLUMN -N3C-2-C74	

REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY
R0	22-06-2026	GOOD FOR CONSTRUCTION	NPS	SAM	SDK

REVISION HISTORY

STRUCTURAL CONSULTANT : PPS ENGINEERING CONSULTANTS LLP.
FIRST FLOOR, SERVICE BUILDING, BAFI BHAVAN, DR. MANISHAI DESAI NAGAR, WARJE, PUNE 411058, INDIA. EMAIL : design@ppspl.in
WEB SITE : www.ppspl.in Tel. : + 91 20 25232858

PROJECT NUMBER : 25-4035

PROJECT NAME : ACXNMI-03














CLIENT : ADANICONNEX












DETAILS OF PRECAST COLUMN : N3C-2-C74

DWG NUMBER	N3C-2-C74-F			
APPROVAL	NAME	DATE	SCALE : AS SHOWN	REV. : R0
TENDER	DRAWN	NPS	22-06-2026	
CONSTRUCTION	CHECKED	SAM	22-06-2026	
INFORMATION	APPROVED	SDK	22-06-2026	

ELEMENT NO.	REQUIRED NO.
N3C-2-C74	01
N3C-2-C61	01
TOTAL	02

DETAILS OF IP2					
PLATE PROFILE	WT OF PLATE / IP IN KG	DIA OF LUGS	NO. OF LUGS / IP	TOTAL LENGTH OF LUGS / IP IN METER	TOTAL LUGS WEIGHT / IP IN KG
250X200X12	4.71	12	3	2.55	2.66

N3C-2-C74 REBAR SCHEDULE											
			BENDING DIMENSIONS								
BAR MARK	BAR DIAMETER	QTY.	BENDING DETAILS	A	B	C	C1	D	BAR CUTTING LENGTH	TOTAL BAR LENGTH	TOTAL WEIGHT
261	10	6		840	0	0		0	840	5100	3.15 kg
4629	10	216		80	786	80		0	946	205200	126.67 kg
4631	10	16		209	830	120		120	2237	36000	22.22 kg
6028	10	2		836	820	836		0	2460	4950	3.06 kg
6155	10	252		160	786	80		80	2003	510300	315.02 kg
6157	12	4		830	830	96		96	3413	13700	12.18 kg
6311	12	5		450	189	312	600	0	1520	7625	6.78 kg
6315	10	2		836	390	836		0	2030	4100	2.53 kg
6517	10	1		840	383	80		80	2556	2575	1.59 kg
6671	10	8		80	830	80		0	957	7800	4.82 kg
6719	10	3		1340	820	80		80	4431	13350	8.24 kg
6894	25	5		200	1319	200		0	1637	8250	31.83 kg
6895	12	5		400	186	292	845	185	2601	13125	11.67 kg
6897	10	1		990	820	80		80	3731	3750	2.31 kg
6914	10	1		1170	820	80		80	4091	4100	2.53 kg
6915	10	1		273	840	80		80	2336	2350	1.45 kg
6916	10	1		362	840	80		80	2514	2525	1.56 kg
6917	10	1		352	840	80		80	2494	2500	1.54 kg

N3C-2-C74 REBAR SCHEDULE											
			BENDING DIMENSIONS								
BAR MARK	BAR DIAMETER	QTY.	BENDING DETAILS	A	B	C	C1	D	BAR CUTTING LENGTH	TOTAL BAR LENGTH	TOTAL WEIGHT
6918	10	1		279	840	80		80	2349	2350	1.45 kg
7555	10	1		1170	450	80		80	3351	3375	2.08 kg
7556	10	1		990	450	80		80	2991	3000	1.85 kg
7557	10	3		1340	450	80		80	3691	11100	6.85 kg
7637	25	5		296	1032	200		0	1446	7250	27.97 kg
7702	10	1		840	248	80		80	2287	2300	1.42 kg
7853	40	16		9221	0	0		0	9221	147600	1457.87 kg
7896	10	1		686	820	686		0	2159	2175	1.34 kg
7897	10	1		686	390	686		0	1729	1750	1.08 kg
7898	10	1		798	820	798		0	2383	2400	1.48 kg
7899	10	1		758	390	758		0	1874	1875	1.16 kg
8107	32	8		8895	0	0		0	8895	71200	458.56 kg
8463	12	72		786	786	96		96	3277	237600	211.21 kg
8464	25	2		776	800	0		0	1534	3100	11.96 kg
8465	25	1		928	800	0		0	1687	1700	6.56 kg
645										1346075	2752.01 kg

N3C-2-C74 REBAR SCHEDULE SUMMARY		
BAR DIAMETER	TOTAL BAR LENGTH	TOTAL WEIGHT
10	834925	515.42 kg
12	272050	241.84 kg
25	20300	78.32 kg
32	71200	458.56 kg
40	147600	1457.87 kg
1346075		2752.01 kg

R0	25-06-2026	GOOD FOR CONSTRUCTION	NPS	SAM	SDK
REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY
REVISION HISTORY					
STRUCTURAL CONSULTANT :		PPS ENGINEERING CONSULTANTS LLP.			
		FIRST FLOOR, SERVICE BUILDING, BAIF BHAVAN, DR. MANIBHAI DESAI NAGAR, WARJE, PUNE 411058, INDIA. EMAIL : design@ppsi.in WEB SITE : www.ppspl.in Tel. : + 91 20 25232558			
PROJECT NUMBER		25-4035			
PROJECT NAME		ACXNMI-03			
		CLIENT			
		ADANICONNEX			
REINFORCEMENT DETAILS OF PRECAST COLUMN :			N3C-2-C74		
DWG NUMBER		N3C-2-C74-RF1			
RELEASED FOR	APPROVAL		NAME	DATE	SCALE : AS SHOWN SIZE : A2 REV. : R0
	TENDER		NPS	25-06-2026	
	CONSTRUCTION	✓	CHECKED	SAM	
	INFORMATION		APPROVED	SDK	
