



MOULD DRAWING(M)

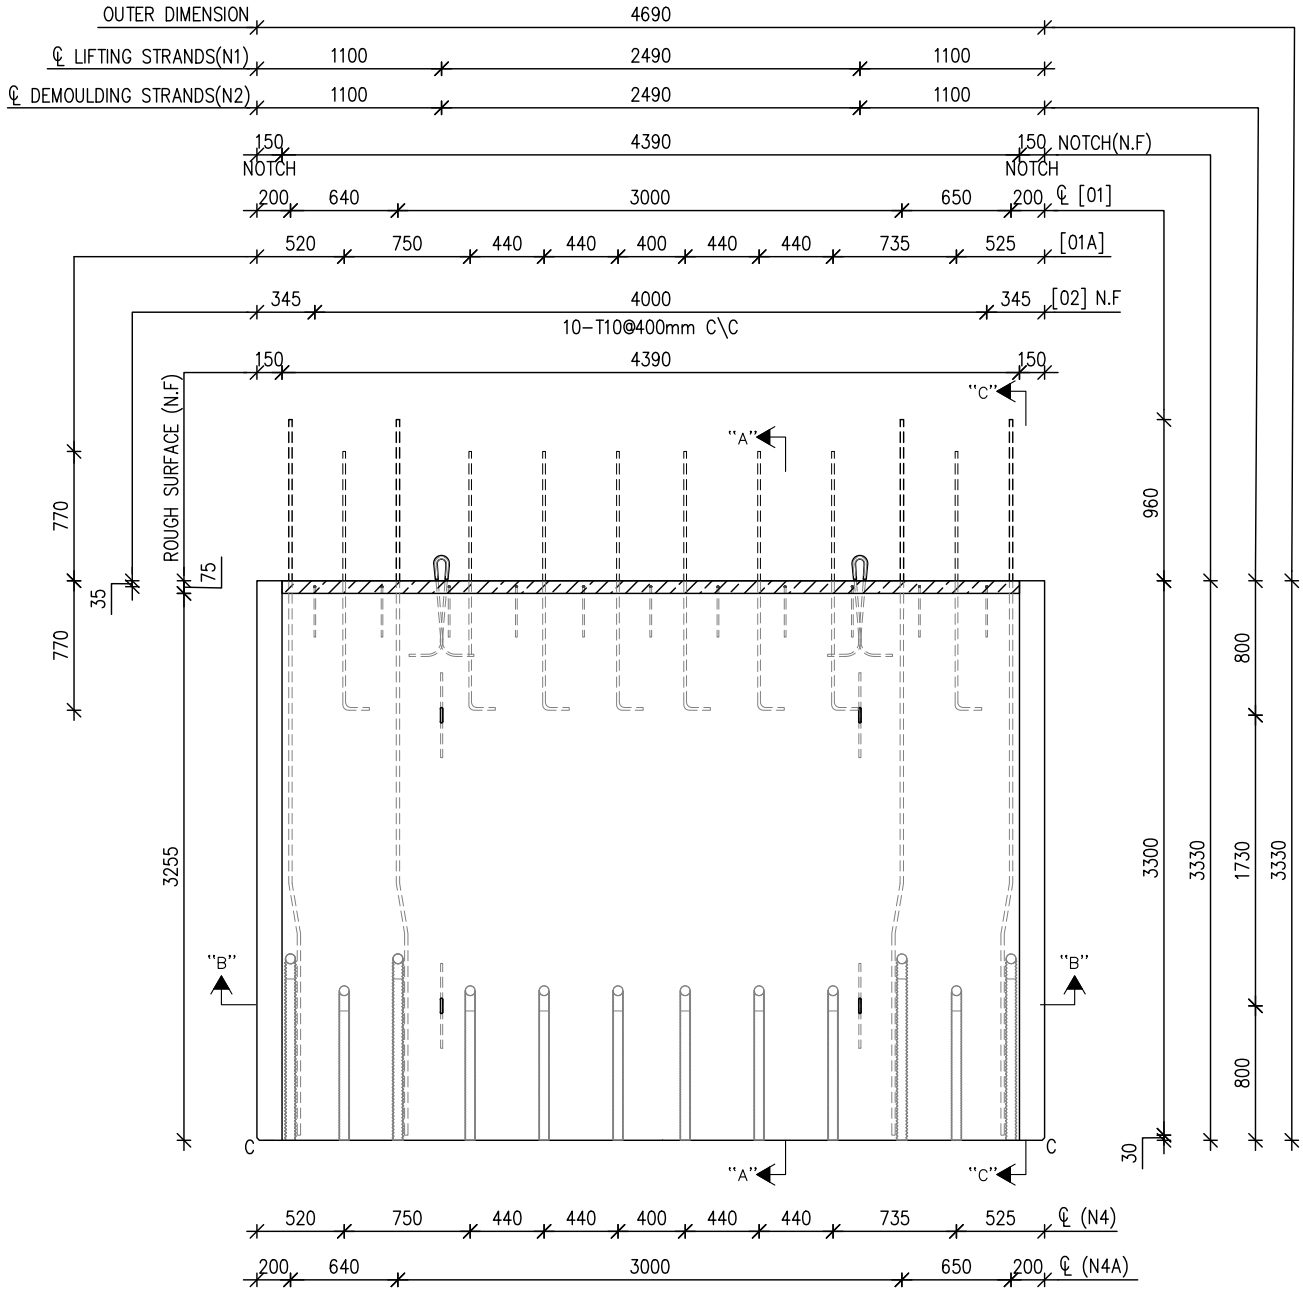


PLAN VIEW
(1:45)

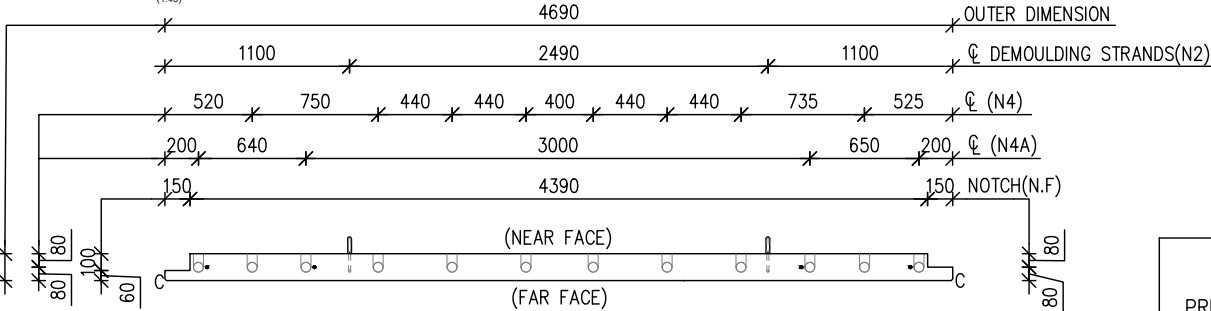


SECTION-B
(1:45)

TYPICAL DEMOULDING DETAILS (N2)




Ø12.9mm Strands for Lifting
(2.0 Ton capacity) @ Each pick point


TYPICAL LIFTING DETAILS (N1)

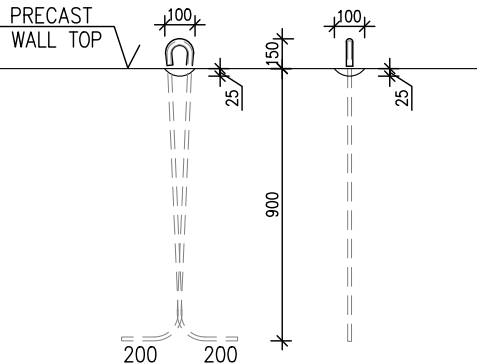

Ø12.9mm Strands for Lifting
(4.00 Ton capacity) @ Each pick point

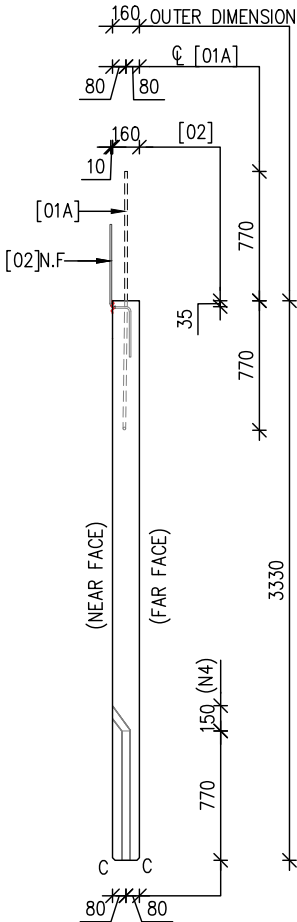

SECTION-A
(1:45)

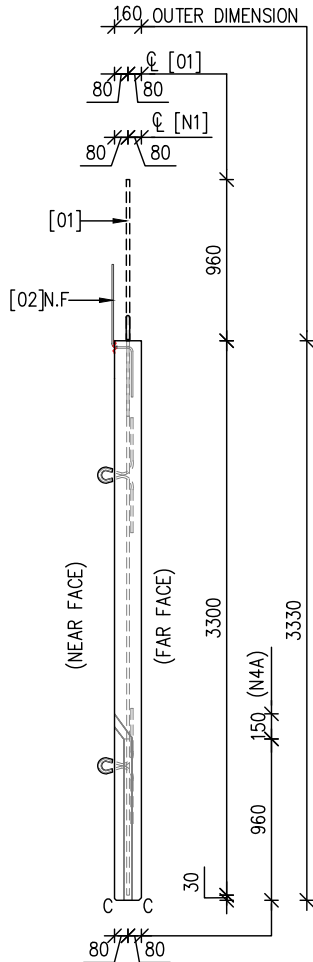

SECTION-C
(1:45)

BLOCK NAME	ELEMENT ID	QTY
EMC PLOT_ACCOMMODATION BLOCK_1	EA1_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_2	EA2_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_3	EA3_1W_08A	01
TOTAL		03

GENERAL NOTES:

- GRADE OF CONCRETE – M40
- CONCRETE STRENGTH
 - AFTER 28 DAYS : 40 MPa
 - DEMOULDING STRENGTH : 18 MPa
- REINFORCEMENT GRADE: HIGH YIELD STRENGTH DEFORMED BARS (Fe550).
- DO NOT SCALE FROM THE DRAWING.
- ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE SPECIFIED.
- PRODUCTION TOLERANCE:
 - LENGTH: ± 5/10MM
 - WIDTH (OVERALL): AS PER PCI MNL-116 AND PCI MNL-135
 - DEPTH/THICKNESS (OVERALL): AS PER PCI MNL-116 AND PCI MNL-135
- ERECTION TOLERANCE: ±10MM WITH RESPECT TO GRID LINE AS PER DRAWING.
- NOMINAL CLEAR COVER: 30MM

ITEM NO:	EA1_1W_08A	QTY:	--
VOLUME:	2.40 Cu.M	WEIGHT:	6.02 Tons
MIN. COVER:	30MM		
REFER DWG:	EA1_1W_08A_R		

INSTALLATION PARTS / MATERIAL CATALOGUE

N0	ACCESSORIES	DESCRIPTION	QTY.
N1	LIFTING STRANDS	4 TON CAPACITY (EACH)	02
N2	DEMOULDING STRANDS	2.0 TON CAPACITY (EACH)	04
N3	WIRE LOOP BOX	PVL-80 LOOP BOX	--
N3A	WIRE LOOP BOX	PVL-120 LOOP BOX	--
N4	CORRUGATED SLEEVES	Ø50MM TUBE	08
N4A	CORRUGATED SLEEVES	Ø50MM TUBE	02

LEGEND:

☒ CUTOUT		C.-CHAMFER
N.F.-NEAR FACE	F.F.-FAR FACE	E.F.-EACH FACE

PRODUCT FINISH:
 TOP SIDE ----- STEEL TROWEL
 FORM SIDE ----- FORM FINISH
 ENDS ----- AS CAST (UNO)
 'C' ----- CHAMFER (10mmx10mm)
 BLOCK AT STRIPPING POINTS FOR STORAGE AND SHIPPING

RO	24-07-2026	ISSUED FOR PRODUCTION	SS	MS	SR
REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY

REVISION HISTORY



CLIENT'S ADDRESS :	PRINCIPAL ARCHITECT:
adani	YANTRA ARC 703, Aalps Euphoria, near by Gota cross road, S.G.highway, Ahmedabad, Gujarat-382481 PH :+91-997-978-2305 Email : mail@yantraarc.in

PROJECT NUMBER	26BLR013
PROJECT NAME	EMC PLOT -WORKMEN ACCOMMODATION BLOCK
BUILDCAST	OWNER BUILDCAST SOLUTIONS PVT. LTD.

TRC ENGINEERING (I) PVT LTD	STRUCTURAL / PRECAST CONSULTANTS: TRC ENGINEERING (I) PVT LTD 108, 4th 'C' Cross, 5th Block, Koramangala Industrial Layout, Bangalore-560095 Ph: 080 6759 3000
---------------------------------------	---

ELEMENT MARK: EA1_1W_08A_M
MOULD DRAWING

RELEASED FOR	APPROVAL	DRN. BY:	CHKD. BY:	APPROVED BY:	REV : R0
CONSTRUCTION	✓	SS	MS	SR	SIZE : A3
INFORMATION					

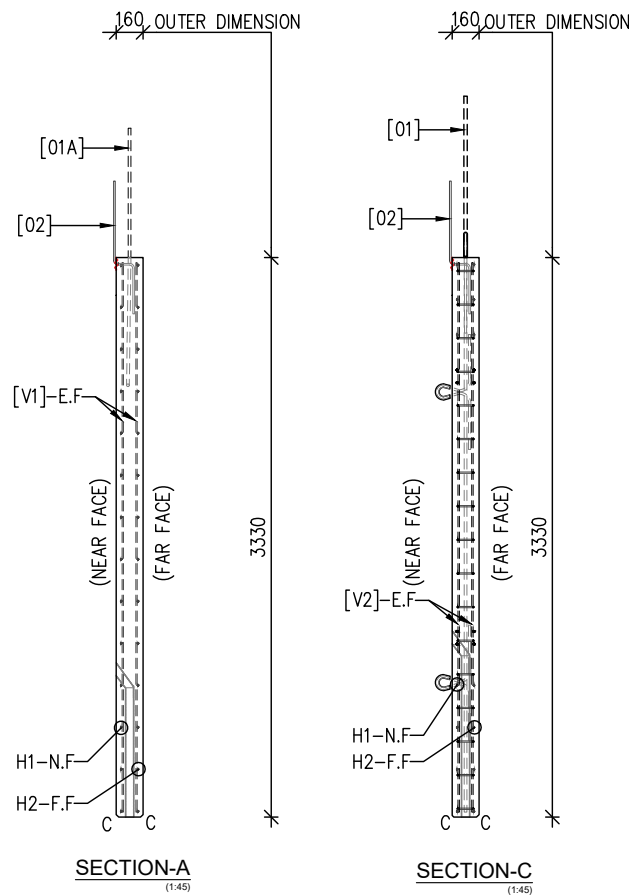

BLOCK NAME	ELEMENT ID	QTY
EMC PLOT_ACCOMMODATION BLOCK_1	EA1_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_2	EA2_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_3	EA3_1W_08A	01
	TOTAL	03

- PRODUCT FINISH:
- TOP SIDE ----- STEEL TROWEL
- FORM SIDE ----- FORM FINISH
- ENDS ----- AS CAST (UNO)
- 'C' ----- CHAMFER (10mmx10mm)
- BLOCK AT STRIPPING POINTS FOR STORAGE AND SHIPPING


RELEASED FOR	APPROVAL		DRN. BY:	CHKD. BY:	APPROVED BY:	REV : R0
	CONSTRUCTION	✓	SS	MS	SR	SIZE : A3
	INFORMATION					

BBS DRAWING(S)

BAR BENDING SCHEDULE/ELEMENT MARK:					EA1_1W_08A								
Bar Mark	Bar Dia. (mm)	Length of Each Bar (mm)	Total No of Bars	Total Bar Length (mm)	Weight Per Unit Length (kg/m)	Total Weight (kg)	Bending Dimensions						Bar Shape Code
							a*	b*	c*	d*	e*	f*	
V1	T8	3270	32	104640	0.395	41.29	3270						SB100
V2	T12	3270	8	26160	0.888	23.23	3270						SB100
H1	T8	4330	14	60620	0.395	23.92	4330						SB100
H2	T8	4630	14	64820	0.395	25.58	4630						SB100
O1	T20	4265	4	17060	2.466	42.07	2760	305	1200				LB114
O1A	T16	1740	8	13920	1.578	21.97	200	1540					LB101
O2	T10	905	11	9955	0.617	6.14	480	125	300				ZB107
O3	T8	860	46	39560	0.395	15.61	250	100	250	100	80	80	STP103
TOTAL -				336.74 m		199.80 kg							

DIAMETER WISE BREAK-UP OF STEEL WEIGHT IN kg

Bar Dia. (mm)	Total Weight (kg)
T8	106.40
T10	6.14
T12	23.23
T16	21.97
T20	42.07
TOTAL	199.80

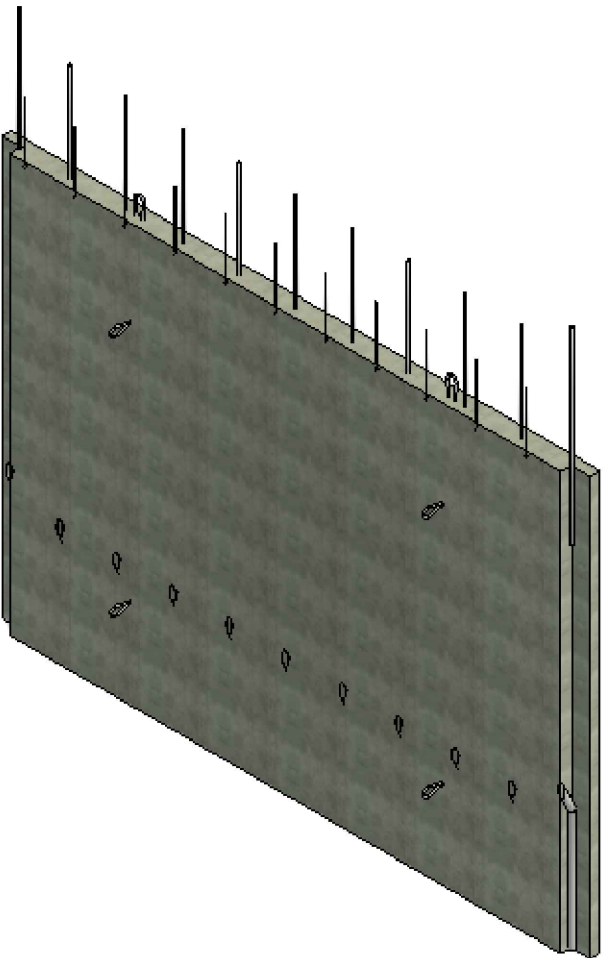

ISOMETRIC VIEW

BAR SHAPE CODE				
SB100	LB101	UB102	STP103	LB106
LB111	LB111A	LB114	LB114A	LHB115
CHB116	CHB116A	ZB107	LB111B	CB118

GENERAL NOTES:

1. GRADE OF CONCRETE – M40
2. CONCRETE STRENGTH

2.1. AFTER 28 DAYS : 40 MPa

2.2. DEMOULDING STRENGTH : 18 MPa
3. REINFORCEMENT GRADE: HIGH YIELD STRENGTH DEFORMED BARS (Fe550).
4. DO NOT SCALE FROM THE DRAWING.
5. ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE SPECIFIED.
6. PRODUCTION TOLERANCE:

6.1. LENGTH: ± 5/10MM

6.2. WIDTH (OVERALL): AS PER PCI MNL–116 AND PCI MNL–135

6.3. DEPTH/THICKNESS (OVERALL): AS PER PCI MNL–116 AND PCI MNL–135
7. ERECTION TOLERANCE: ±10MM WITH RESPECT TO GRID LINE AS PER DRAWING.
8. NOMINAL CLEAR COVER: 30MM

ITEM NO:	EA1_1W_08A	QTY:	--
----------	------------	------	----

VOLUME: 2.40 Cu.M	WEIGHT: 6.02 Tons	MIN. COVER:	30MM
-------------------	-------------------	-------------	------

REFER DWG:	EA1_1W_08A_R
------------	--------------

INSTALLATION PARTS / MATERIAL CATALOGUE			
---	--	--	--

NO	ACCESSORIES	DESCRIPTION	QTY.
N1	LIFTING STRANDS	4 TON CAPACITY (EACH)	02
N2	DEMOULDING STRANDS	2.0 TON CAPACITY (EACH)	04
N3	WIRE LOOP BOX	PVL–80 LOOP BOX	--
N3A	WIRE LOOP BOX	PVL–120 LOOP BOX	--
N4	CORRUGATED SLEEVES	ø50MM TUBE	08
N4A	CORRUGATED SLEEVES	ø50MM TUBE	02

LEGEND:					
☒ CUTOUT		C.–CHAMFER			
N.F.–NEAR FACE	F.F.–FAR FACE	E.F.–EACH FACE			

PRODUCT FINISH:
TOP SIDE ----- STEEL TROWEL
FORM SIDE ----- FORM FINISH
ENDS ----- AS CAST (UNO)
'C' ----- CHAMFER (10mmx10mm)
BLOCK AT STRIPPING POINTS FOR STORAGE AND SHIPPING

R0	24-07-2026	ISSUED FOR PRODUCTION	SS	MS	SR
REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY

REVISION HISTORY					
CLIENT'S ADDRESS : 			PRINCIPAL ARCHITECT: 703, Aalps Euphoria, near by Gota cross road, S.G.highway, Ahmedabad, Gujarat-382481 PH : +91-997-978-2305 Email : mail@yantraarc.in		

PROJECT NUMBER	26BLR013
PROJECT NAME	EMC PLOT -WORKMEN ACCOMMODATION BLOCK
	OWNER
	BUILDCAST SOLUTIONS PVT. LTD.

	STRUCTURAL / PRECAST CONSULTANTS:
	TRC ENGINEERING (I) PVT LTD 108, 4th 'C' Cross, 5th Block, Koramangala Industrial Layout, Bangalore-560095 Ph: 080 6759 3000

ELEMENT MARK: EA1_1W_08A_S BBS DRAWING					
---	--	--	--	--	--

RELEASED FOR	APPROVAL		DRN. BY:	CHKD. BY:	APPROVED BY:	REV : R0 SIZE : A3
	CONSTRUCTION	✓	SS	MS	SR	
	INFORMATION					

BLOCK NAME	ELEMENT ID	QTY
EMC PLOT_ACCOMMODATION BLOCK_1	EA1_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_2	EA2_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_3	EA3_1W_08A	01
TOTAL		03

MEP DRAWING(MEP)

MEP NOTES		
Sl.No.	DESCRIPTION	Qty.
1.	2M METAL BOX	05
2.	6M METAL BOX	04
3.	ELBOW	06

GENERAL NOTES:

- GRADE OF CONCRETE – M40
- CONCRETE STRENGTH
 - AFTER 28 DAYS : 40 MPa
 - DEMOULDING STRENGTH : 18 MPa
- REINFORCEMENT GRADE: HIGH YIELD STRENGTH DEFORMED BARS (Fe550).
- DO NOT SCALE FROM THE DRAWING.
- ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE SPECIFIED.
- PRODUCTION TOLERANCE:
 - LENGTH: ± 5/10MM
 - WIDTH (OVERALL): AS PER PCI MNL-116 AND PCI MNL-135
 - DEPTH/THICKNESS (OVERALL): AS PER PCI MNL-116 AND PCI MNL-135
- ERECTION TOLERANCE: ±10MM WITH RESPECT TO GRID LINE AS PER DRAWING.
- NOMINAL CLEAR COVER: 30MM

ITEM NO:	EA1_1W_08A	QTY:	--
VOLUME:	2.40 Cu.M	WEIGHT:	6.02 Tons
		MIN. COVER:	30MM
REFER DWG:	EA1_1W_08A_R		

INSTALLATION PARTS / MATERIAL CATALOGUE

N0	ACCESSORIES	DESCRIPTION	QTY.
N1	LIFTING STRANDS	4 TON CAPACITY (EACH)	02
N2	DEMOULDING STRANDS	2.0 TON CAPACITY (EACH)	04
N3	WIRE LOOP BOX	PVL-80 LOOP BOX	--
N3A	WIRE LOOP BOX	PVL-120 LOOP BOX	--
N4	CORRUGATED SLEEVES	ø50MM TUBE	08
N4A	CORRUGATED SLEEVES	ø50MM TUBE	02

LEGEND:

☒ CUTOUT		C.-CHAMFER
N.F.-NEAR FACE	F.F.-FAR FACE	E.F.-EACH FACE

PRODUCT FINISH:
TOP SIDE ----- STEEL TROWEL
FORM SIDE ----- FORM FINISH
ENDS ----- AS CAST (UNO)
'C' ----- CHAMFER (10mmx10mm)
BLOCK AT STRIPPING POINTS FOR STORAGE AND SHIPPING

RO	24-07-2026	ISSUED FOR PRODUCTION	SS	MS	SR
REV.	DATE	DRAWING STATUS	DRAWN BY	CHECKED BY	APPROVED BY

REVISION HISTORY


CLIENT'S ADDRESS :	PRINCIPAL ARCHITECT:
	 YANTRA ARC 703, Aalps Euphoria, near by Gota cross road, S.G.highway, Ahmedabad, Gujarat-382481 PH : +91-997-978-2305 Email : mail@yantraarc.in

PROJECT NUMBER	26BLR013
PROJECT NAME	EMC PLOT -WORKMEN ACCOMMODATION BLOCK
	OWNER
	BUILDCAST SOLUTIONS PVT. LTD.


	STRUCTURAL / PRECAST CONSULTANTS:
	TRC ENGINEERING (I) PVT LTD 109, 4th 'C' Cross, 5th Block, Koramangala Industrial Layout, Bangalore-560095 Ph: 080 6759 3000

ELEMENT MARK:	EA1_1W_08A MEP MEP DRAWING
---------------	-------------------------------

RELEASED FOR	APPROVAL	DRN. BY:	CHKD. BY:	APPROVED BY:	REV : R0
	CONSTRUCTION	SS	MS	SR	SIZE : A3
	INFORMATION				

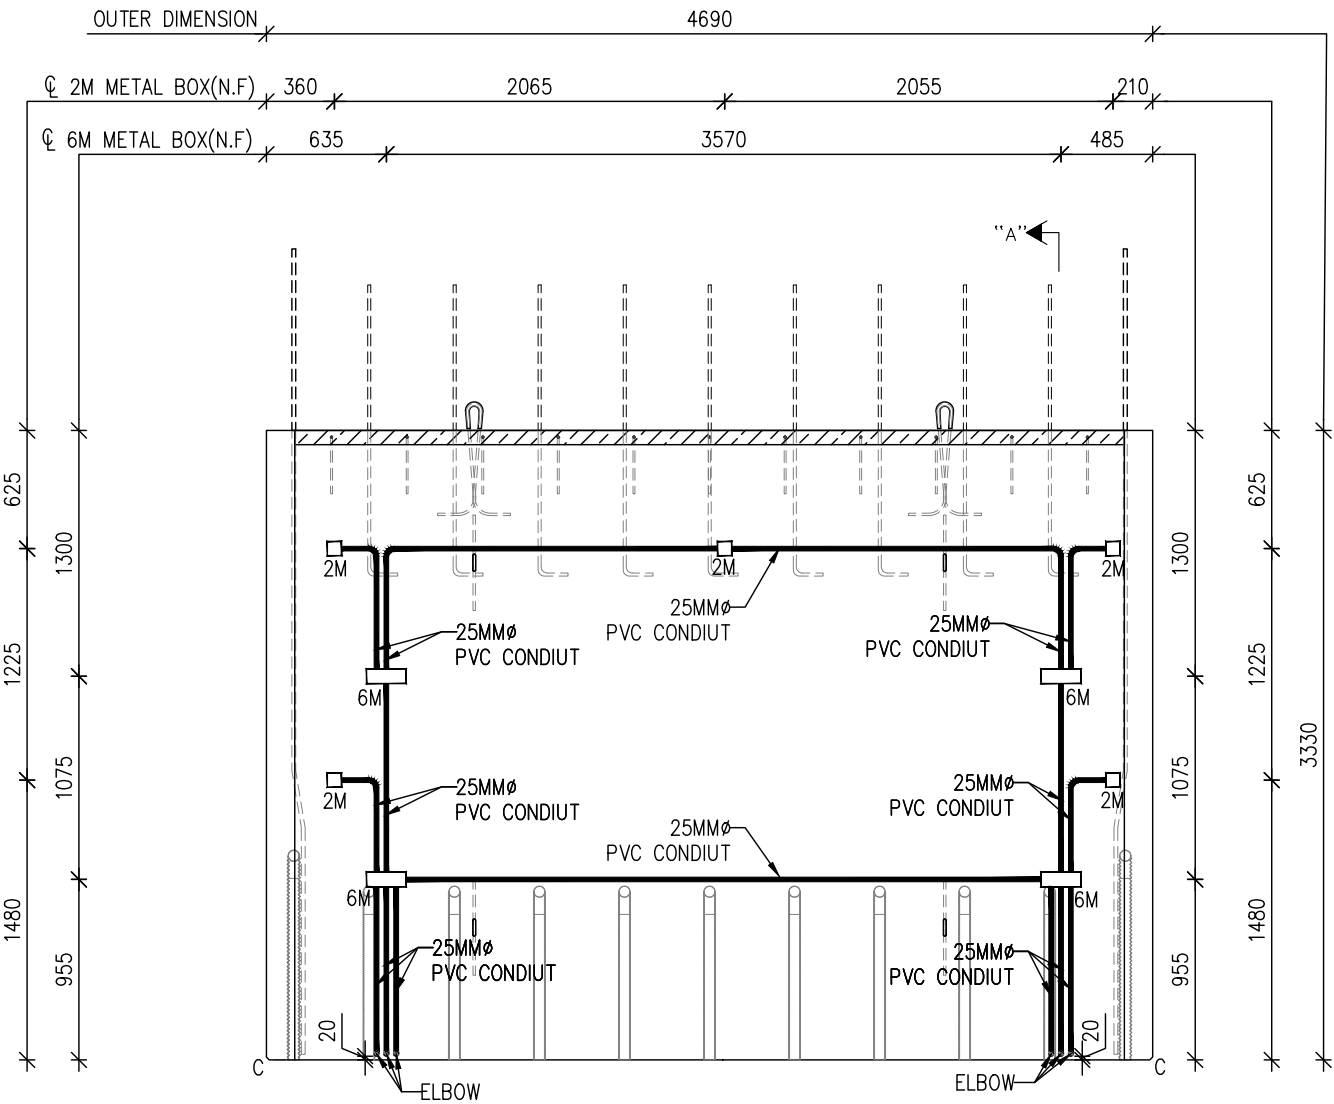

PLAN VIEW
(1:45)

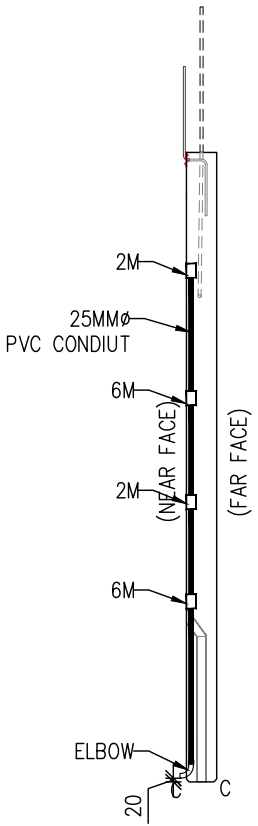

SECTION-A
(1:45)

BLOCK NAME	ELEMENT ID	QTY
EMC PLOT_ACCOMMODATION BLOCK_1	EA1_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_2	EA2_1W_08A	01
EMC PLOT_ACCOMMODATION BLOCK_3	EA3_1W_08A	01
	TOTAL	03
